



EUROPEAN CENTRAL BANK

EUROSYSTEM

TIPS 2025 releases

Candidate change
requests and initiatives

19 April 2024



Agenda

1 Candidate change requests and initiatives

2 Next steps


Candidate change requests and initiatives

Based on the analysis of the business value assignment and keeping in view a **balanced approach**, the idea is to **identify group of Change requests and Initiatives** that should be further explored (let us call them **candidates** for scope) to enable a decision on final scope of June / Nov 2025 releases.

For the candidate **Change requests**, depending on their current status, the next logical step should be triggered (e.g., **initiation of detailed assessment** in view of 2025 release scoping)

For the candidate **Initiatives**, the next step is to (i) **analyse the initiatives further**, (ii) **draft a CR** and (iii) proceed with the CR review followed by the Detailed Assessment (DA).

Once the DA of candidate change requests and DA of change requests drafted for initiatives are available, a **feasibility assessment** can be done to determine what can be scoped in to 2025 releases.

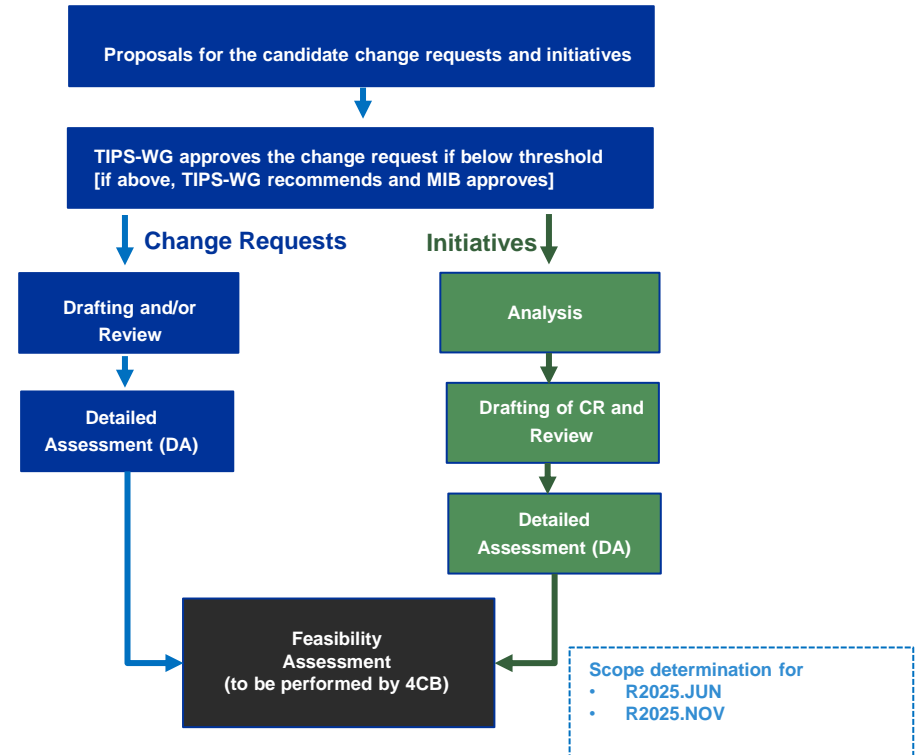

Candidate change requests and initiatives

Candidates Change Requests:

To have in mind for 2025 Releases:

- **Change request already allocated to a November release:**
 - [TIPS-0028-URD - Rule-based liquidity transfer orders between MCA and TIPS DCA](#) >> **R2025.NOV** (aligned with T2)
- **Change request to be drafted following the feedback to be received:**
 - **Following the Instant Payments Regulation (IPR) & EPC Evolution of the EPC payment schemes: SCT Inst scheme adaptations change request(s)**
 - waiting for the European Payments Council (EPC) information on the content of the to-be-updated SCT Inst scheme & expected delivery (ad-hoc release or not)
 - updated version of the SCT Inst scheme rulebook will be published in November 2024 for implementation in November 2025
 - **SEK/DKK change requests:**
 - **Full compliance to Nordic Payments Council (NPC) Instant Credit Transfer Scheme Rulebook**
 - **Change request on Updates of TIPS Directory file for SEK Community**

Candidate change requests and initiatives

Candidates Change Requests (CR):

* Ranking between CRs only

BV Ranking *	CR ID	CR Name	Current status	TIPS Participant impact?	TIPS Release Proposal
1	TIPS-0074-SYS	Automatic simulator enhancements	DA under preparation	Optional for users	R2025.JUN but no deployment in PROD as such as it is linked to testing >> proposal to have all requirements deployed at the same time EAC & in CERT, based on EAC timeline, i.e. in January 2025
2	TIPS-0076-XXX OPTION 2	Verification of payee service with TIPS offering the algorithm on behalf of the beneficiary PSP to do the matching >> this would also include routing (i.e. Option 1) → based on VoP Scheme: "Routing and Verification Mechanism" actor	CR (one or two CRs) to be drafted	Optional for users	Regular release or ad-hoc release to be confirmed >> /\ No Implementation Guidelines (IGs) published by the EPC yet >> according to the Instant Payments Regulation (IPR), PSPs must implement VoP solution by 9 October 2025
3	TIPS-0014-URD	Broadcasts	DA approved	Optional for users	R2025.JUN
4	TIPS-0071-SYS	Quicker communication during non-standard support hours	PA under preparation	Optional for users	R2025.JUN

Candidate change requests and initiatives

Candidates Change Requests:

* Ranking between CRs only

BV Ranking *	CR ID	CR Name	Current status	TIPS Participant impact?	TIPS Release Proposal
5	TIPS-0075-URD	Full compliance with OCT-Inst scheme	CR to be drafted	Optional for users	R2025.NOV >> to check updated scheme to be published by the EPC in November 2024
8	TIPS-0041-URD	Introduction of non-time critical (NTC) instant payments in TIPS	DA under preparation	Optional for users	R2025.NOV
NA	TIPS-0028-URD	Rule-based liquidity transfer orders between MCA and TIPS DCA	DA approved	Yes	R2025.NOV >> together with related T2 change request
NA	N.A	Change request to be drafted following the feedback to be received: <ul style="list-style-type: none"> SCT Inst scheme adaptations/updates change requests Full compliance to Nordic Payments Council (NPC) Instant Credit Transfer Scheme Rulebook Change request on Updates of TIPS Directory file for SEK Community 	CRs to be drafted	Yes	R2025.NOV or earlier if EPC ad-hoc release

Candidate change requests and initiatives

Candidates Change Requests:

* Ranking between CRs only

The following CRs are **not considered as candidate CRs for 2025 scoping:**

BV Ranking *	CR ID	CR Name	Current status	TIPS Participant impact?	Reason for not being in the preliminary scope
7	TIPS-0046-SYS OPTION 1	Resend TIPS Reports via “fully-fledged” implementation	PA approved	Optional for users	On hold >> 2022, 2023 and Jan/Feb 2024 statistics on how many times PSPs required a re-send and average turnaround time by 4CB Service Desk: from go-live to date, about 10 resend requests per year to which, on average, 4CB Service Desk responded on the next BD
9	TIPS-0069-SYS	camt.050 leading and trailing blanks	DA under preparation	Yes	On hold >> recent issue raised?
10	TIPS-0016-SYS	Distinction of CERT and PROD environment in PDF from CRDM_TIPS	DA to be started	Yes	On hold >> to be possibly part of a future GUI harmonisation change request
12	TIPS-0008-URD	CMB limit utilisation reset	CR to be adjusted	Optional for users	Requirements of the CR to be discussed with interested CBs (DK, DE and NOK) >> depending on the outcome of the discussion and re-drafting, the CR could be part of 2025 TIPS Release
NA	TIPS-0073-SYS	Removal of the Participation Type from TIPS Directory	DA under preparation	Yes	When change to Directory takes place (e.g. in R2025.NOV if with TIPS-0041-URD)

Candidate change requests and initiatives

Candidates Initiatives:

* Ranking between initiatives only

BV Ranking*	Initiative Name	Comment	TIPS Release Proposal
1	TIPS beyond the euro: Cross-currency for TIPS hosted currencies	TIPS-0065 change request to be drafted	R2025.NOV >> pilot to start afterwards
2	TIPS beyond the euro: Establish links with other IP platforms	Currently this initiative is under monitoring and evaluation. Once finalised, the CR will be drafted in due time	Not before R2026.NOV
3	SEPA Request to Pay (SRTP)		On hold
4	TIPS beyond the euro: European IP Hub	Currently this initiative is under monitoring and evaluation. Once finalised, the CR will be drafted in due time	Not before R2026.NOV

* Ranking between Initiatives only

Agenda

1 Candidate change requests and initiatives

2 **Next steps**

Next steps

- For the candidate change requests :
 - If the change request is not drafted yet and if we have the elements to draft it or to receive the draft, to draft/share it as soon as possible
 - For the candidate change requests scoped for TIPS2025.JUN, to get the detailed assessment as soon as possible in order to launch the Feasibility Assessment for this release

- For the candidate initiative:
 - To finalise the analysis and to draft the related change request

- Once all the DAs are available, the Feasibility Assessment (FA) is performed by the TIPS Service provider; this will confirm the scopes of the releases

Thank you for your attention!



tips@ecb.europa.eu

www.ecb.europa.eu/paym

ECB: market infrastructure and payments
